

Rural Municipality of East St. Paul Bottomley Creek Bank Remediation and Permanent Dike Construction Update - July 8th to July 15th, 2017

Work Performed:

- Removal of the existing dike at 1040 and 1030 Highland Park Drive began.
- Organic material below the dike at 1040 Highland Park Drive was removed.
- Clay fill was placed for the new dike behind the gabion baskets at 1030 Highland Park Drive.
- Culverts through the new dike were installed at 3154 Henderson Highway.
- The foundation for the segmental block wall was completed at 3154 Henderson Highway.

Photographs:



Photo 1 - Removal of the existing dike at 1030 Highland Park Drive.



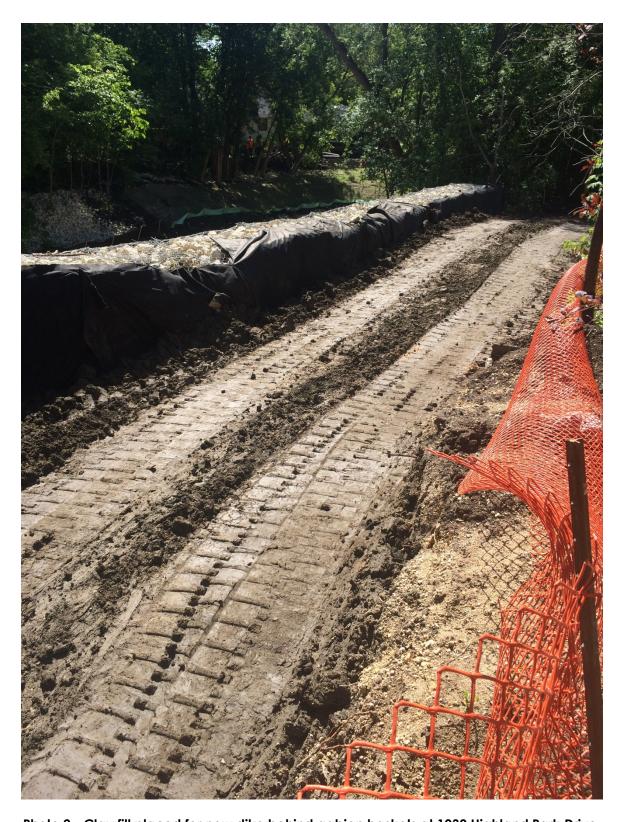


Photo 2 - Clay fill placed for new dike behind gabion baskets at 1030 Highland Park Drive.





Photo 3 - Organic material removed below footprint of new dike at 1040 Highland Park Drive.





Photo 4 - Culvert installed at 3154 Henderson Highway and foundation for segmental block wall completed.





Photo 5 - Culvert installed at 3154 Henderson Highway and foundation for segmental block wall completed.
